
MEASURE G BOND QUARTERLY REPORT

CASINO FAJARDO

DIRECTOR OF CONSTRUCTION AND MODERNIZATION

PRESENTED TO THE BOARD OF EDUCATION:

May 21, 2019

MEASURE G PROJECT LIST (SERIES B)

School / Project	Board Approved Budget 2017	Current Committed Costs	% complete	2019				2020			
				Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Britton Middle School Transformation	\$49,078,449	\$33,370,239	41%	[Gantt chart bars for 2019 and 2020]							
Nordstrom Elementary School	\$10,500,000	\$8,583,469	1%	[Gantt chart bars for 2019 and 2020]							
Jackson Academy of Math and Music Technology	\$12,000,000	\$110,084	1%	[Gantt chart bars for 2019 and 2020]							
Programming & Project Management (thru Dec 2021)	\$5,500,000	\$617,920	11%	[Gantt chart bars for 2019 and 2020]							
Programming & Project Management (thru Dec 2021)	\$2,921,551	\$1,818,692	22%	[Gantt chart bars for 2019 and 2020]							
Series B Total Budgets	\$80,000,000	\$44,500,404	15%								


Series B Proceeds from Bond Sales	\$80,000,000
Interest (through April 2019)	\$1,474,535
Reimbursements	\$0
Series B Total Proceeds	\$81,474,535
Program Contingency	

* Interest accrued identified to fund safety and security updates to campuses

BRITTON MIDDLE SCHOOL MODERNIZATION PROJECT

Increments currently under construction:

- Site work
- Phase 1
- Phase 2

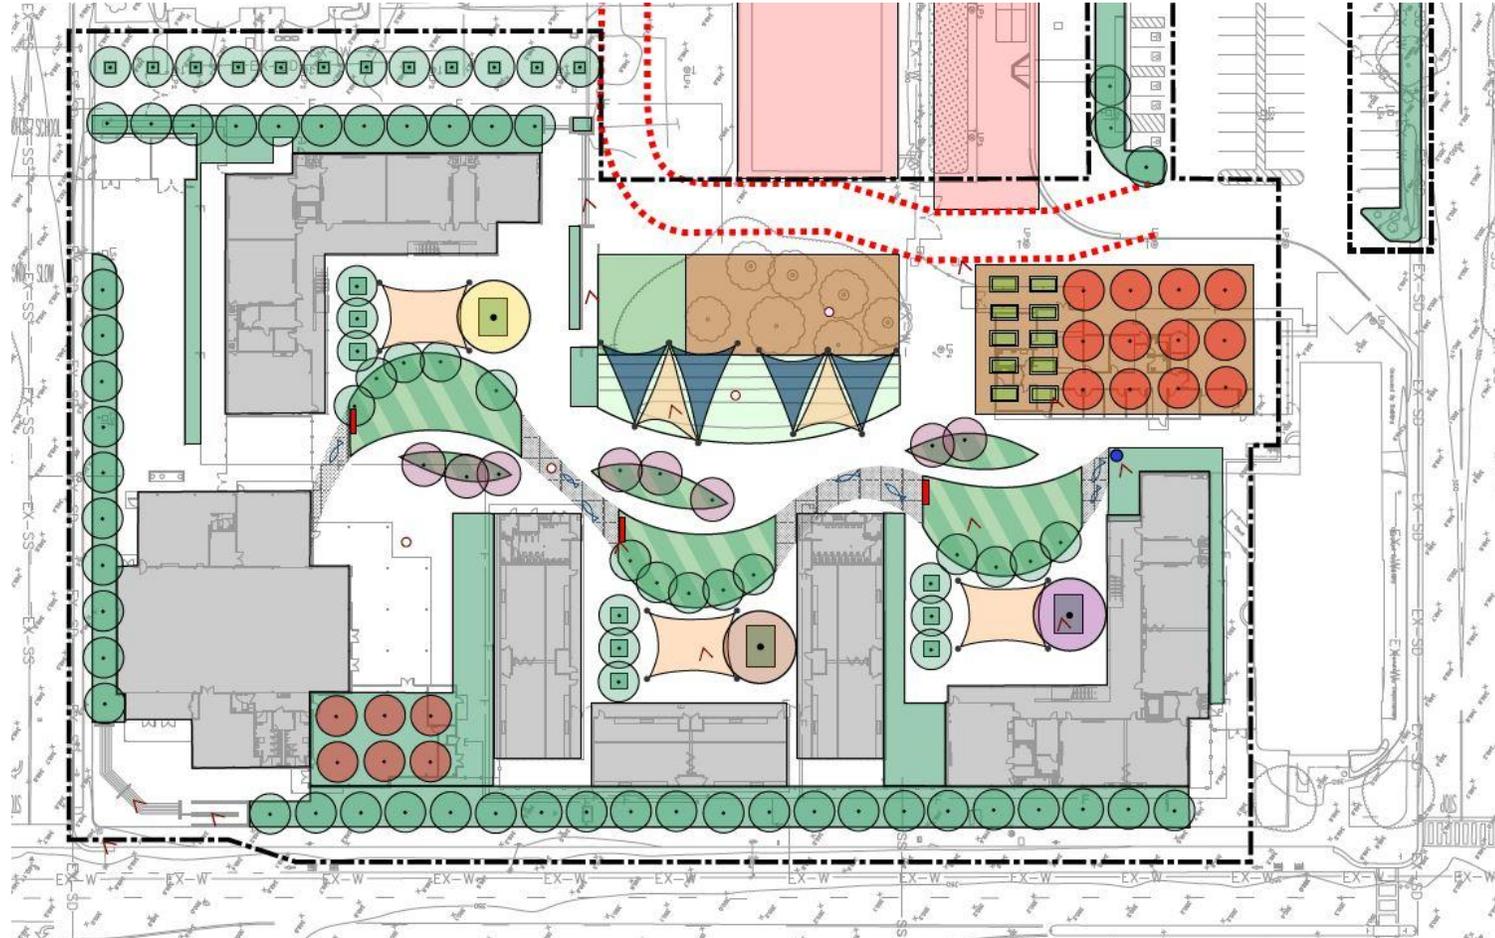

BRITTON MIDDLE SCHOOL MODERNIZATION PROJECT

Increments currently under construction:


- Two-story buildings
 - August 2019

Increment in DSA review:

- Science buildings

Increment in value engineering design:

- Student Union/Admin

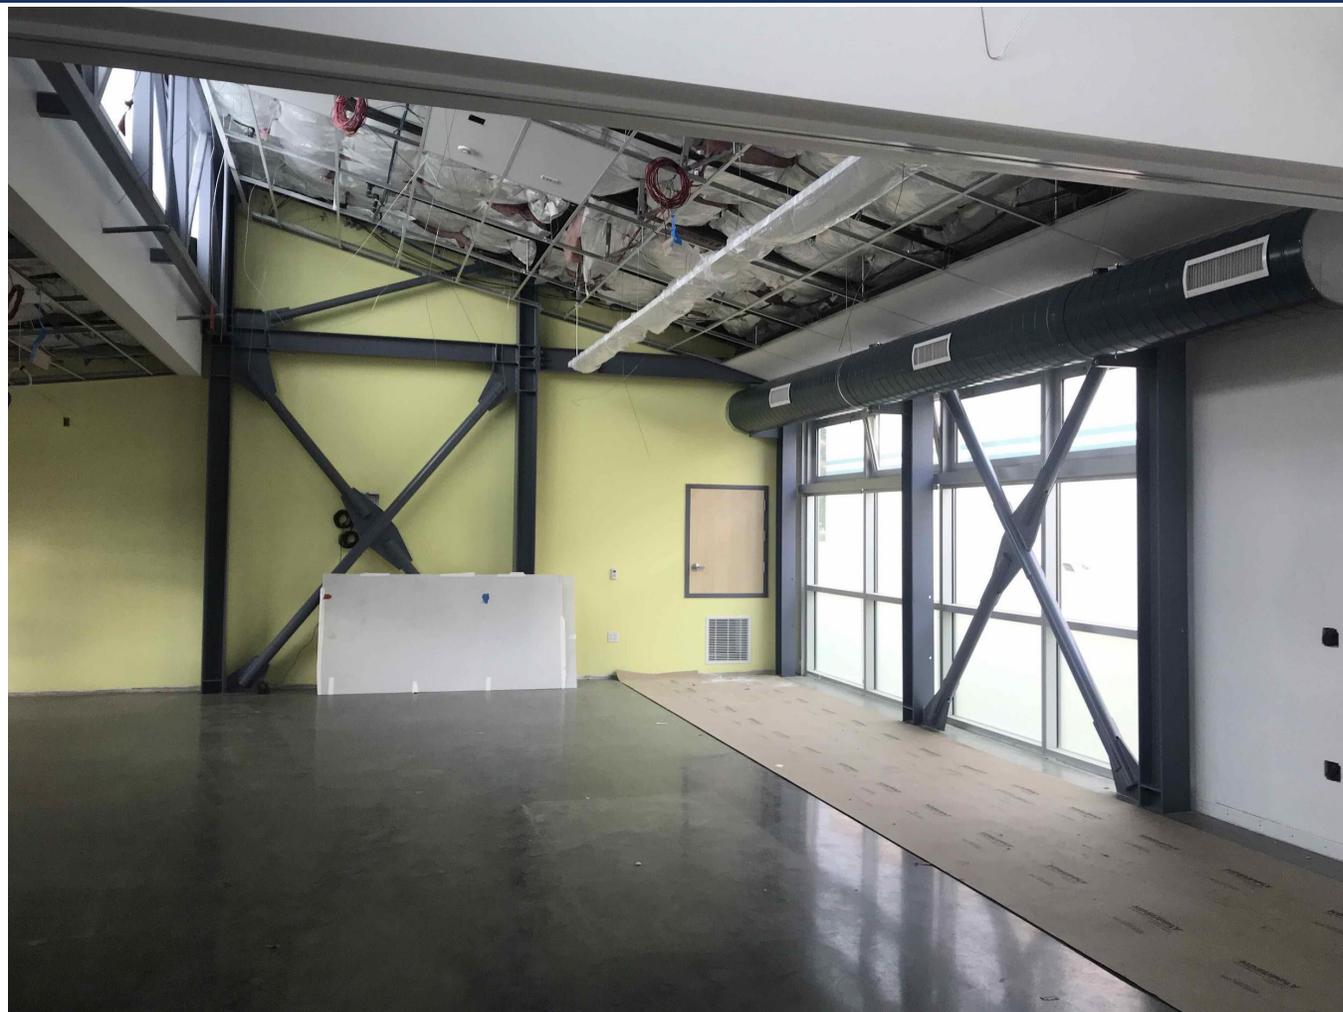

ADDITIONAL CURRENT BOND PROJECTS

1. Paradise Valley Admin - Substantially complete
2. Paradise Valley MUB - Substantially complete
3. Nordstrom - Schematic design complete
4. Jackson - Programming complete
5. Technology - District-wide staff technology refresh started.
 - a. Educator devices, audio visual, classroom devices in progress



SUMMER DEFERRED MAINTENANCE PROJECTS

- Barrett
 - New carpet for eight classrooms
- El Toro
 - Exterior painting
- Los Paseos
 - Upgrading ornamental fencing along the front of campus
 - Principal's office configuration
- Live Oak
 - Administration office roof replacement
- Sobrato
 - Locker room re-plumbing



GRANT OPPORTUNITIES

- Full-Day Kindergarten Facilities Grant Program
Assembly Bill 1808
 - March not awarded, resubmitting in May 2019
- PG&E Electric Vehicle Charging Network
 - Britton was awarded grant by PG&E
- Proposition 51 State Facilities Program
 - Paradise Valley & Britton submitted
 - Submission of potentially Nordstrom & Jackson
- Proposition 51 Career Technical Ed Facilities Program
 - While passing score, not awarded due to area type for the pathway
 - Planning to submit Live Oak and Sobrato next cycle



FACILITIES MASTER PLANNING & FUNDING IDENTIFICATION

- 2020 General Obligation Bond
 - District staff have received proposals and performed initial interviews with political strategist firms regarding the potential 2020 general obligation bond
 - Timeline would be to identify a potential pollster and move forward with strategic planning in June
- Facilities Master Plan
 - Staff are continuing to deliver projects that align with vision outlined in the FMP
 - Staff are working to document current successes in Measure G and will update the FMP with the projects completed



MORGAN HILL UNIFIED SCHOOL DISTRICT FACILITIES MASTER PLAN

September 2017

LPA

60 South Market Street, Suite 150
San Jose, CA 95113
408.780.7200 | www.lpainc.com





QUESTION AND ANSWER
